



Goal 2

Core Network Infrastructure is Nearing 75% Complete at Data Center 3

Frankie Jackson toured with Paula Ross, Director of Networks Infrastructure and Communications, and Mike Raspet, Network Management Operations Network Analyst, in Data Center 3 on Thursday, **August 13, 2015**. Becky Cook, Director of Instructional Technology, also joined the tour. Paula and Mike provided a status of the upgrade, which can be viewed in youtube (see to the right).

YouTube




[Data Center 3 - Tour](#)

Tyndall Overby, eVolve's project manager, provided the following status of the overall Data Center 3 upgrade.



- Centerpoint is the biggest unknown. They are responsible for the new electrical service and have yet to provide definitive timeframe for completion.
- Excluding Centerpoint, upon removal of the existing cabinets there is approximately 2-3 weeks of work remaining to complete Mechanical, Electrical, Plumbing and raised flooring.
- Once CFISD completes the transfer of existing IT load from the existing UPS/PDU to the new UPS, there is approximately 2-3 weeks to demo existing electrical, demo existing wall between DC and print room, build new floor to deck demising wall and new raised flooring in this area.
- Once the relocation of existing MDF and reconfiguring of existing Row "C", two post racks will take 2-3 weeks.
- Once all equipment is in place and connected/operational, installation of the Elert Monitoring system will take about 2-3 weeks to bring online.

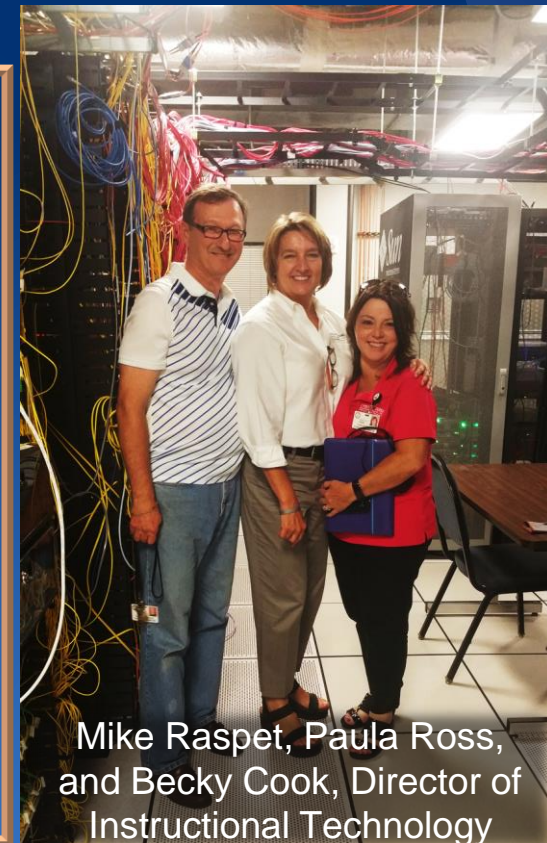

Mike Raspet, Paula Ross, and Becky Cook, Director of Instructional Technology
