




Goal 2

Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

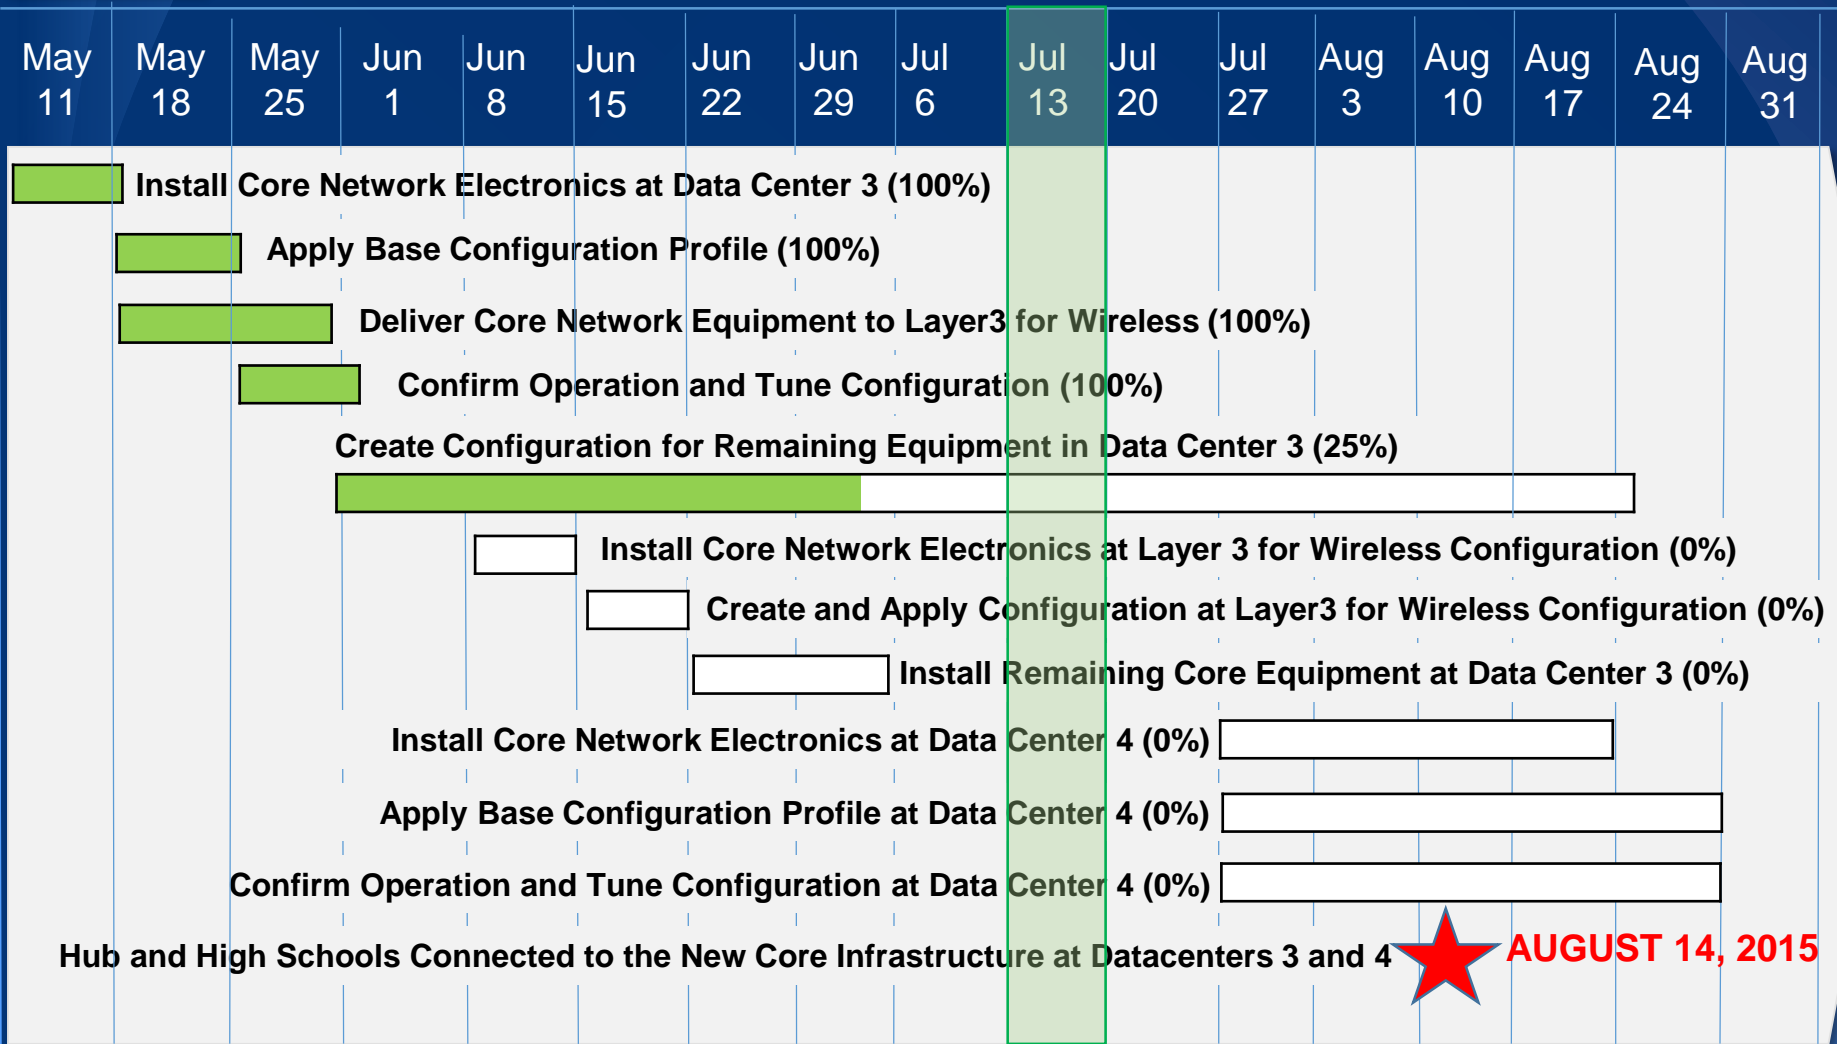


AUGUST 14, 2015





Goal 2


Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

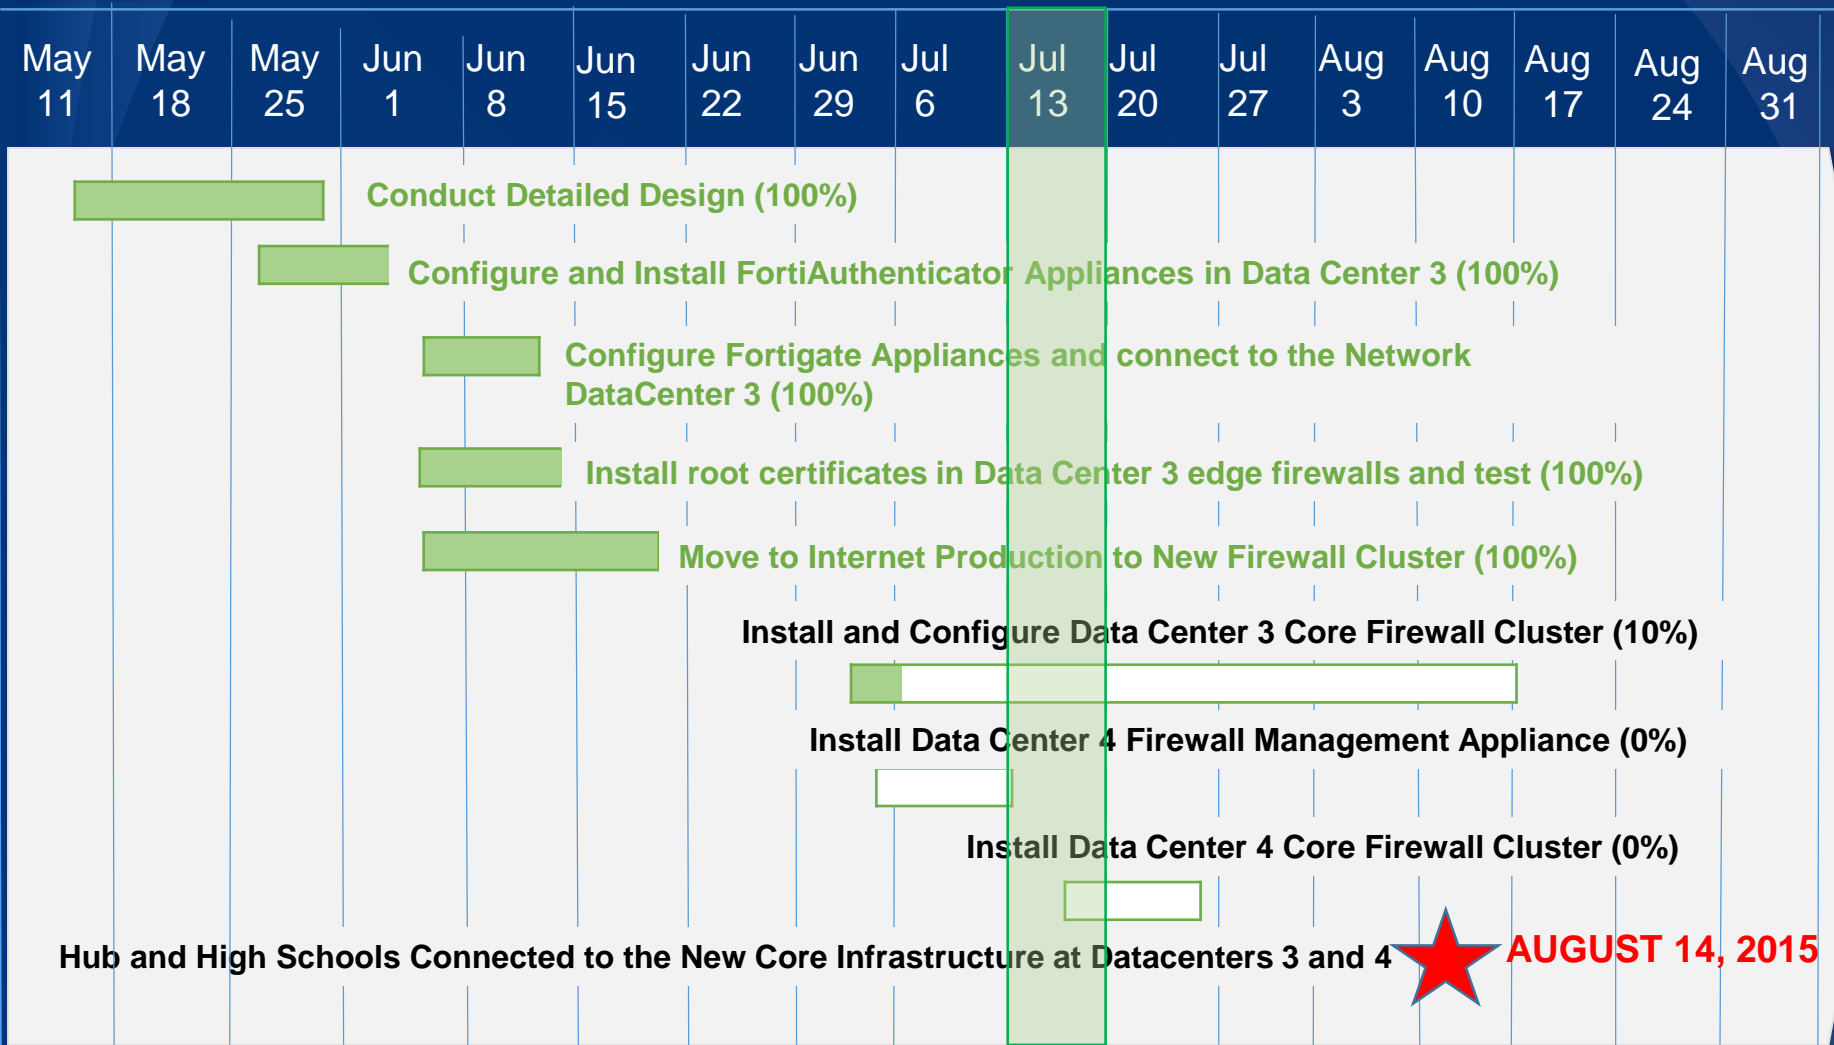



Goal 2

Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

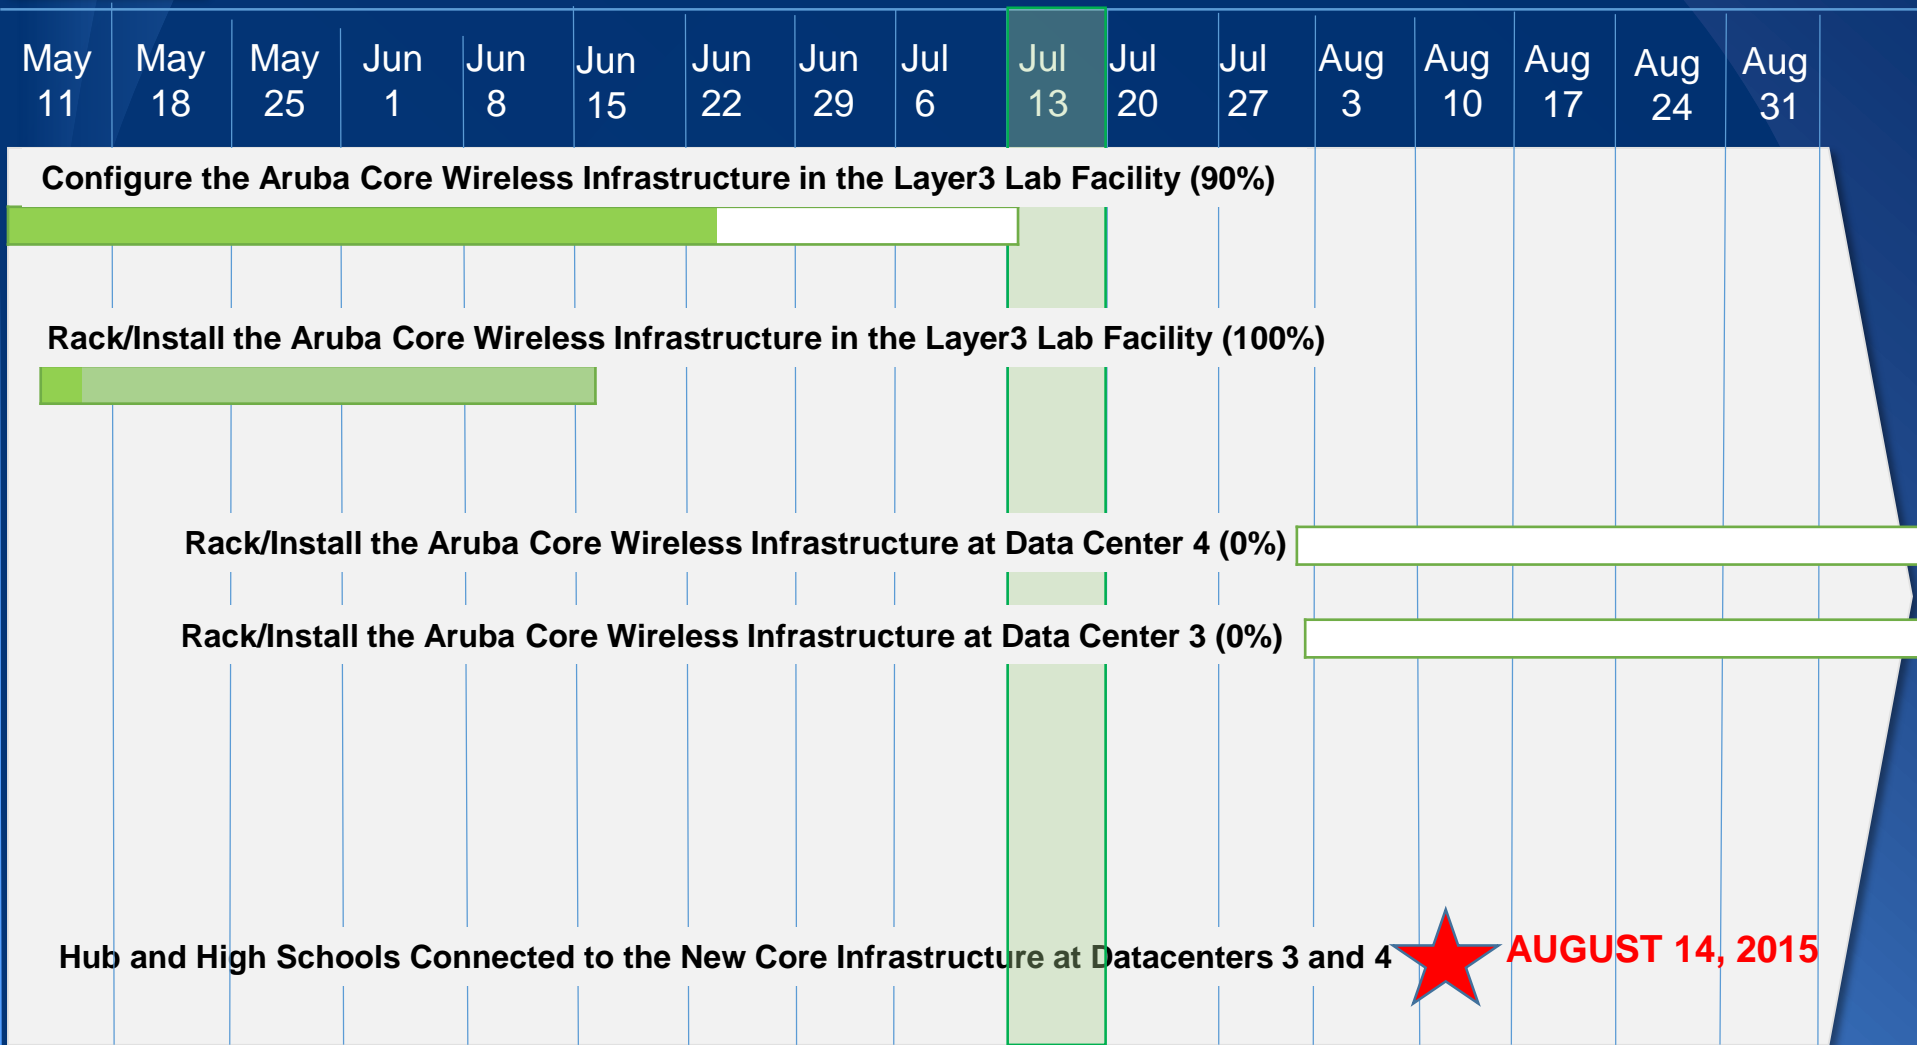


 **AUGUST 14, 2015**





Goal 2


Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

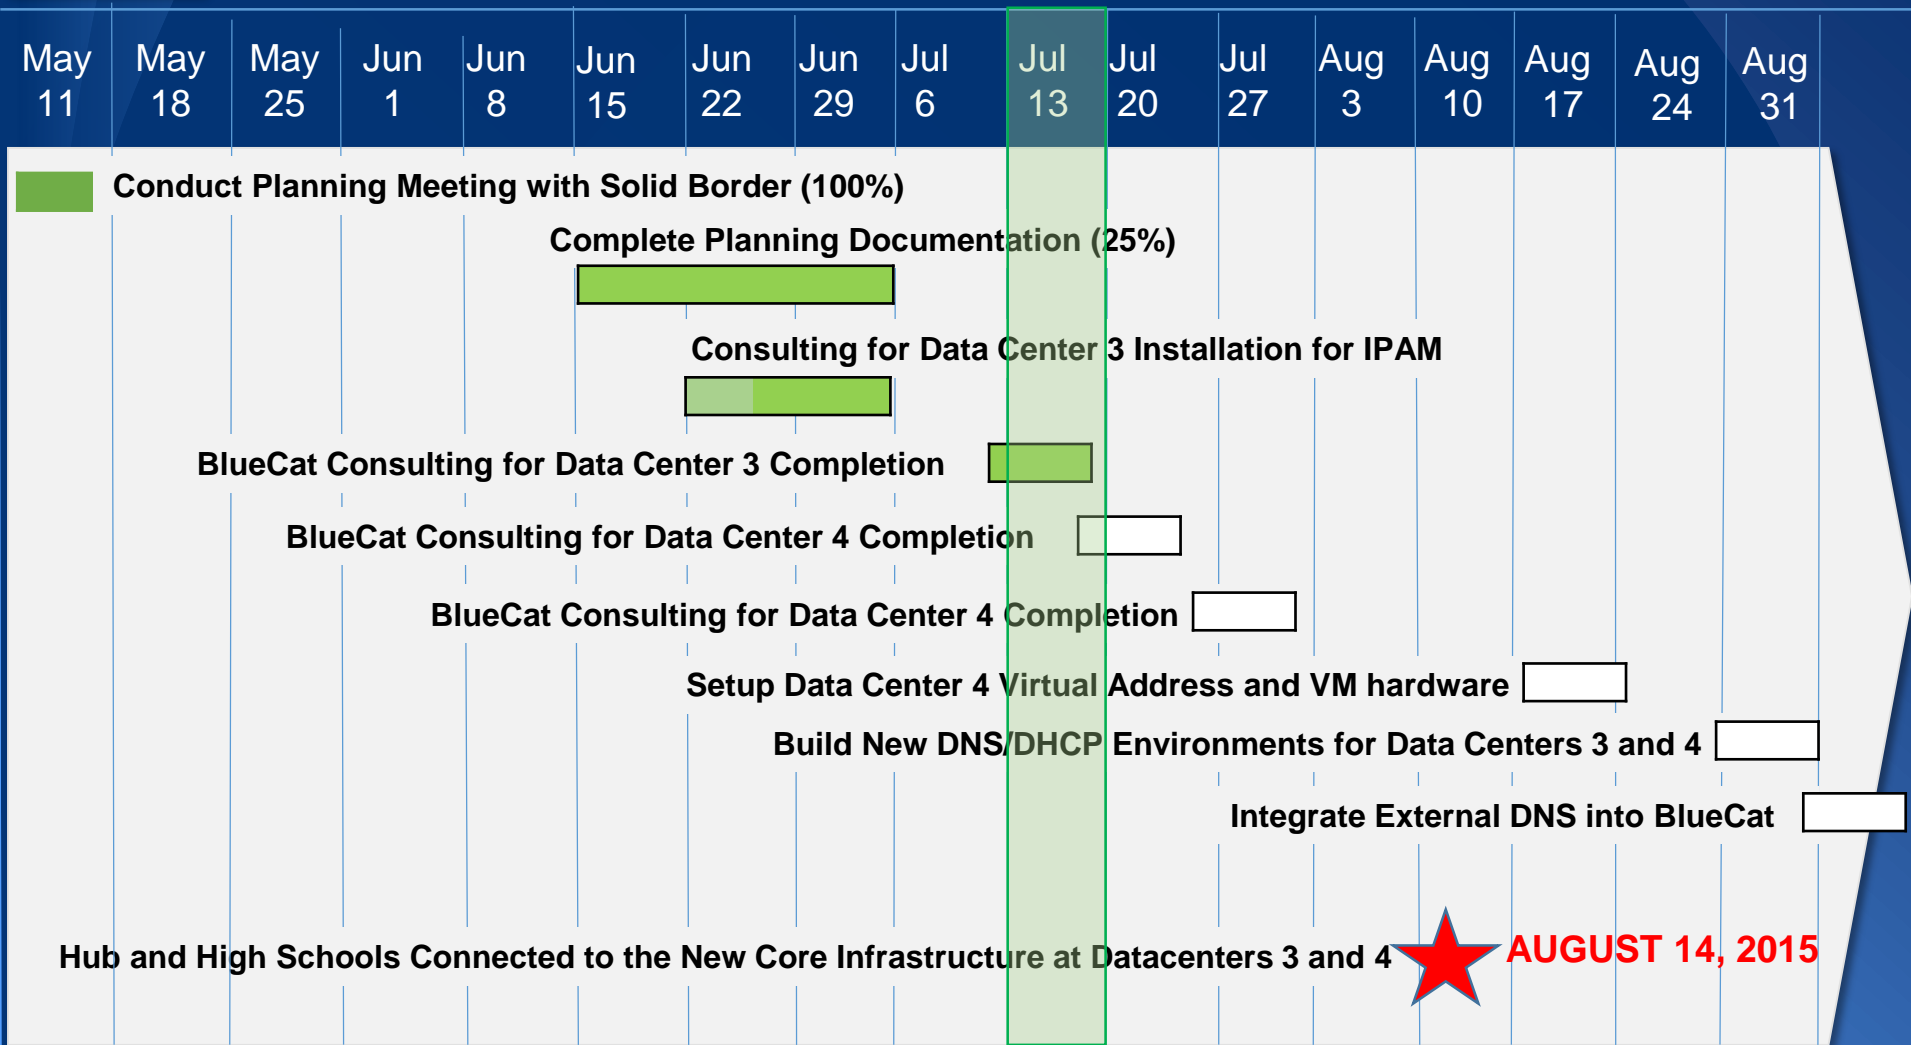



Goal 2


Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

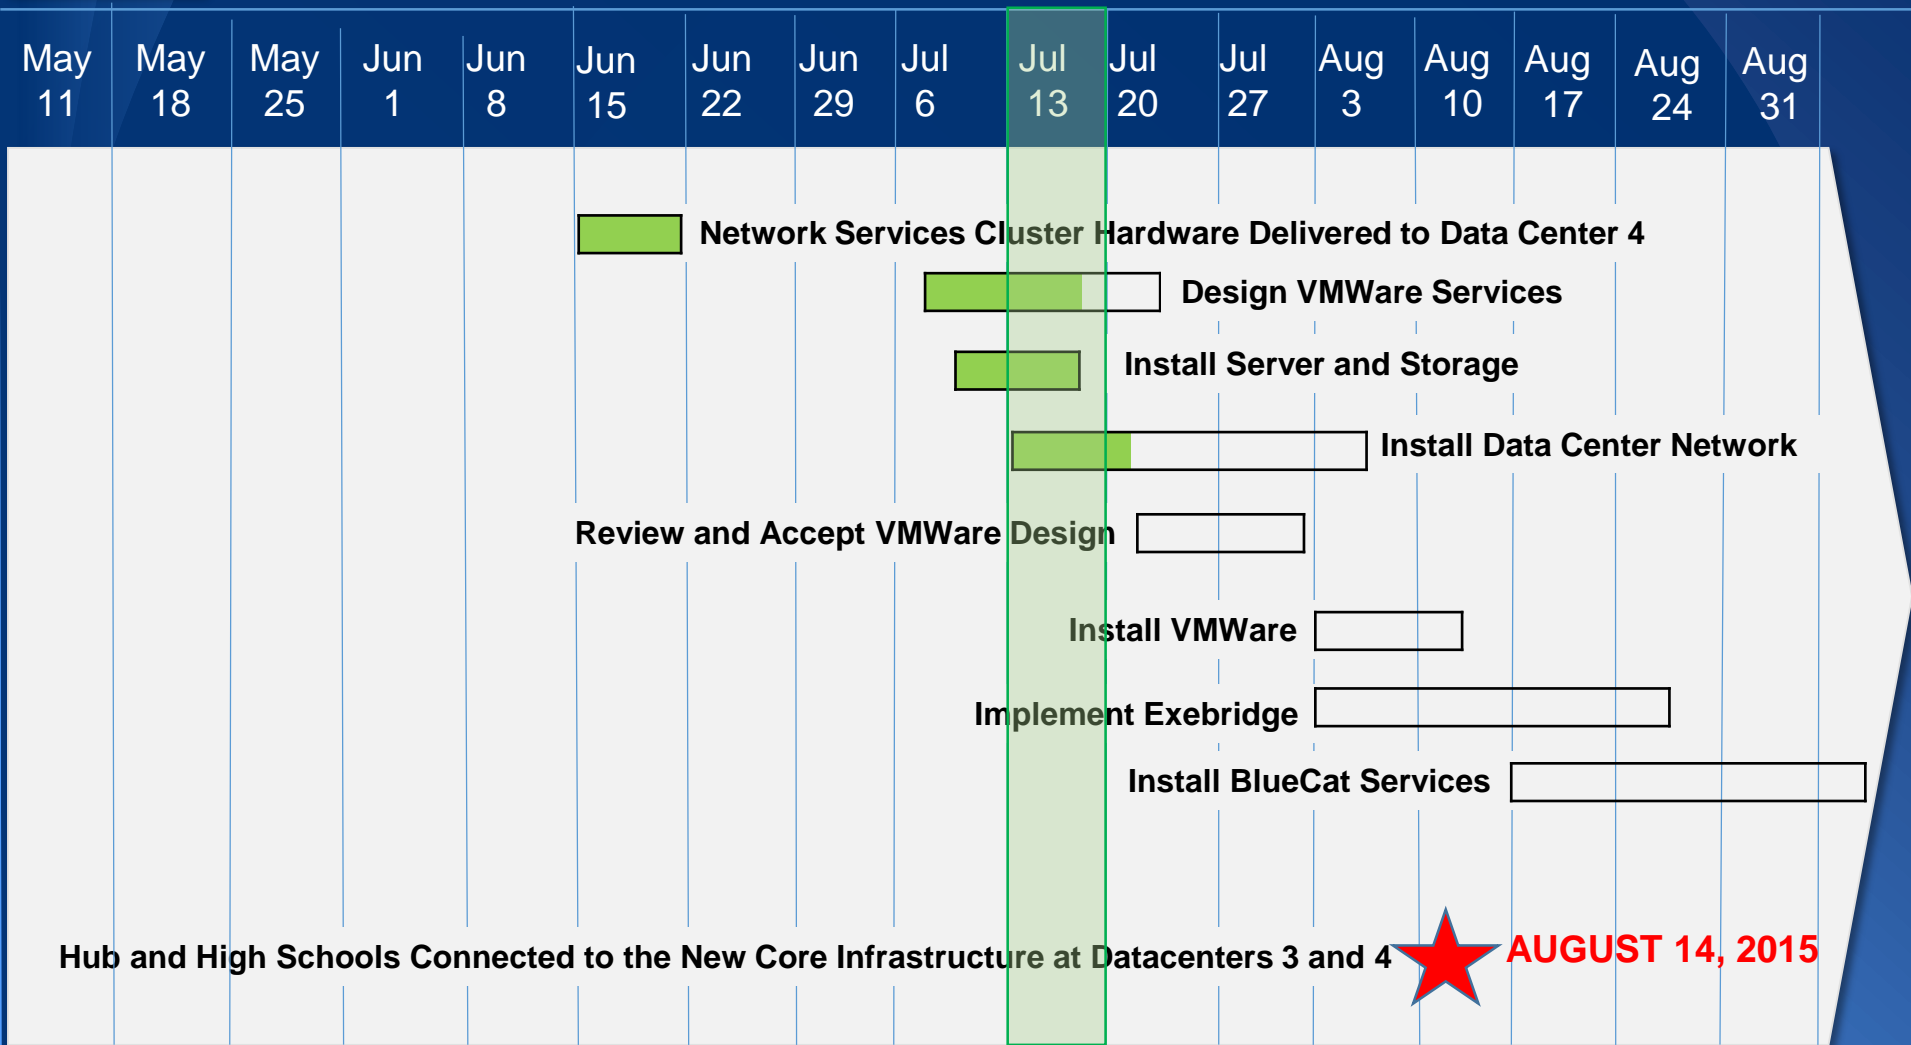



Goal 2


Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

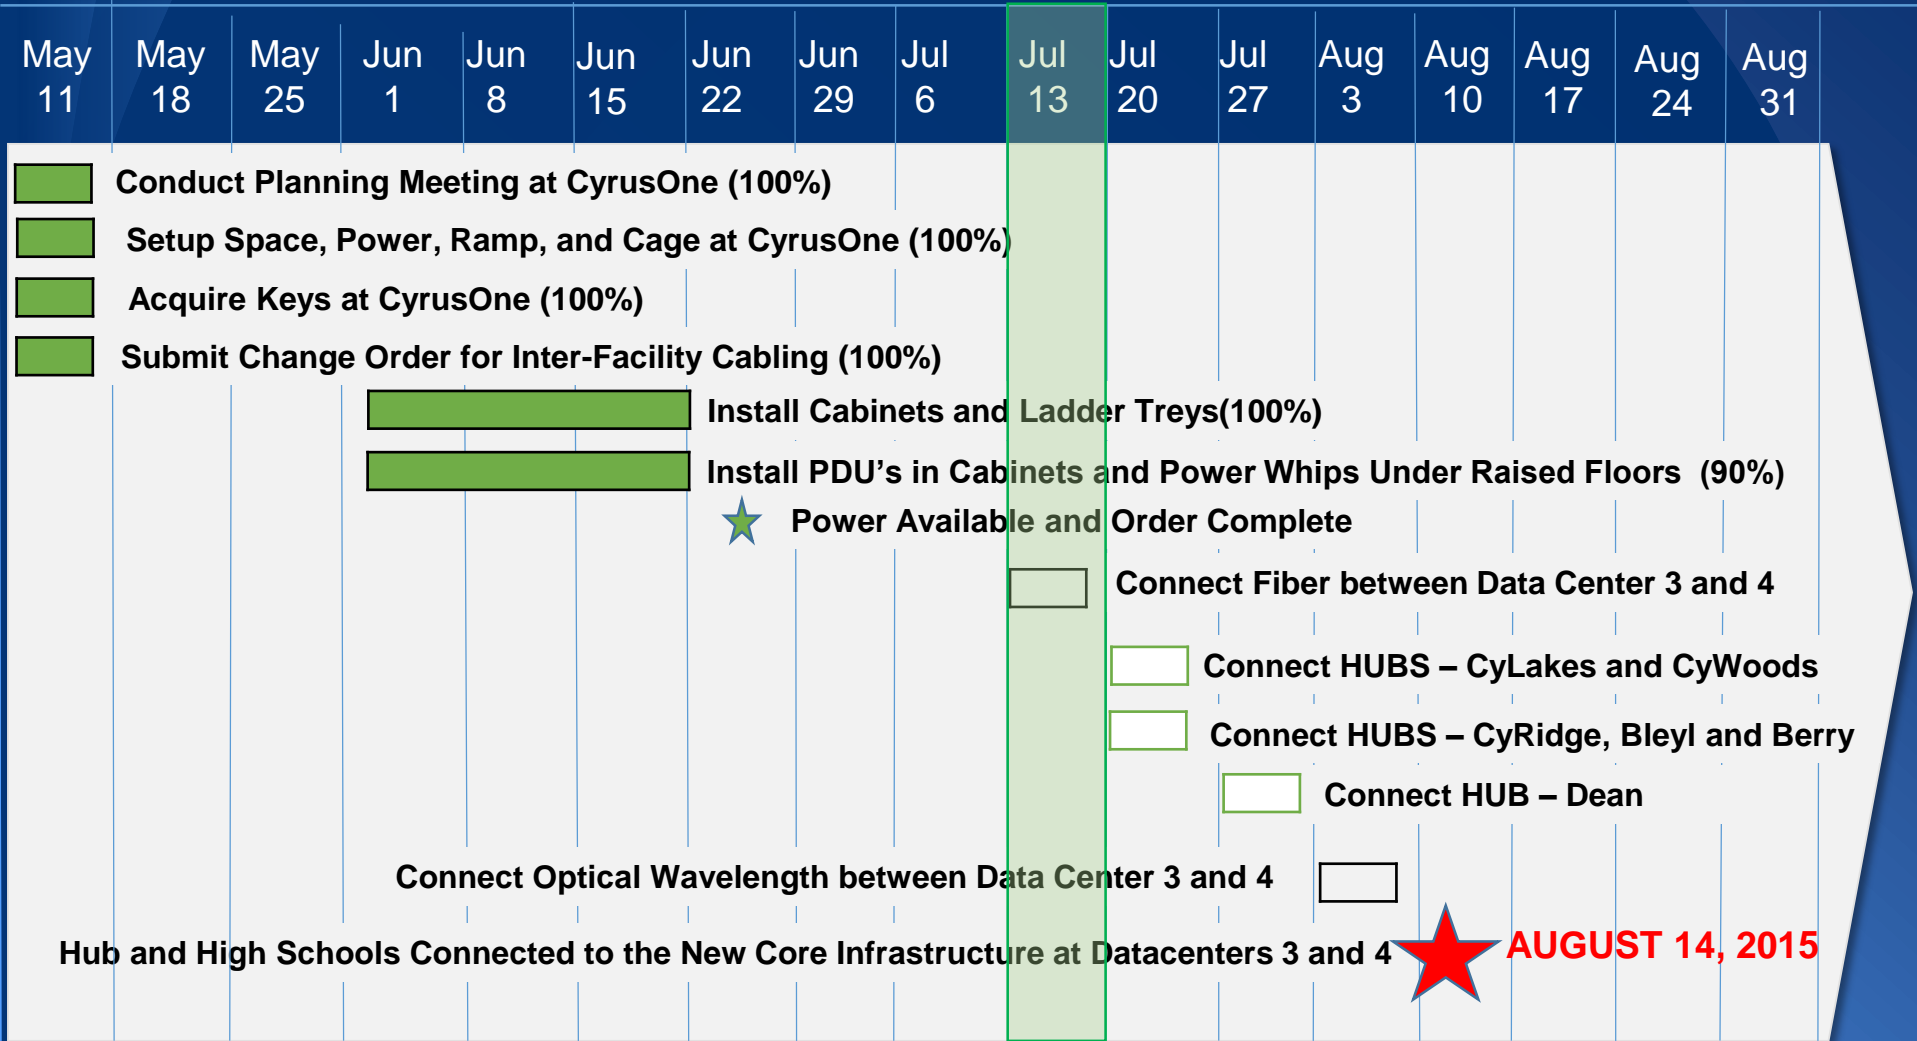



Goal 2

Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

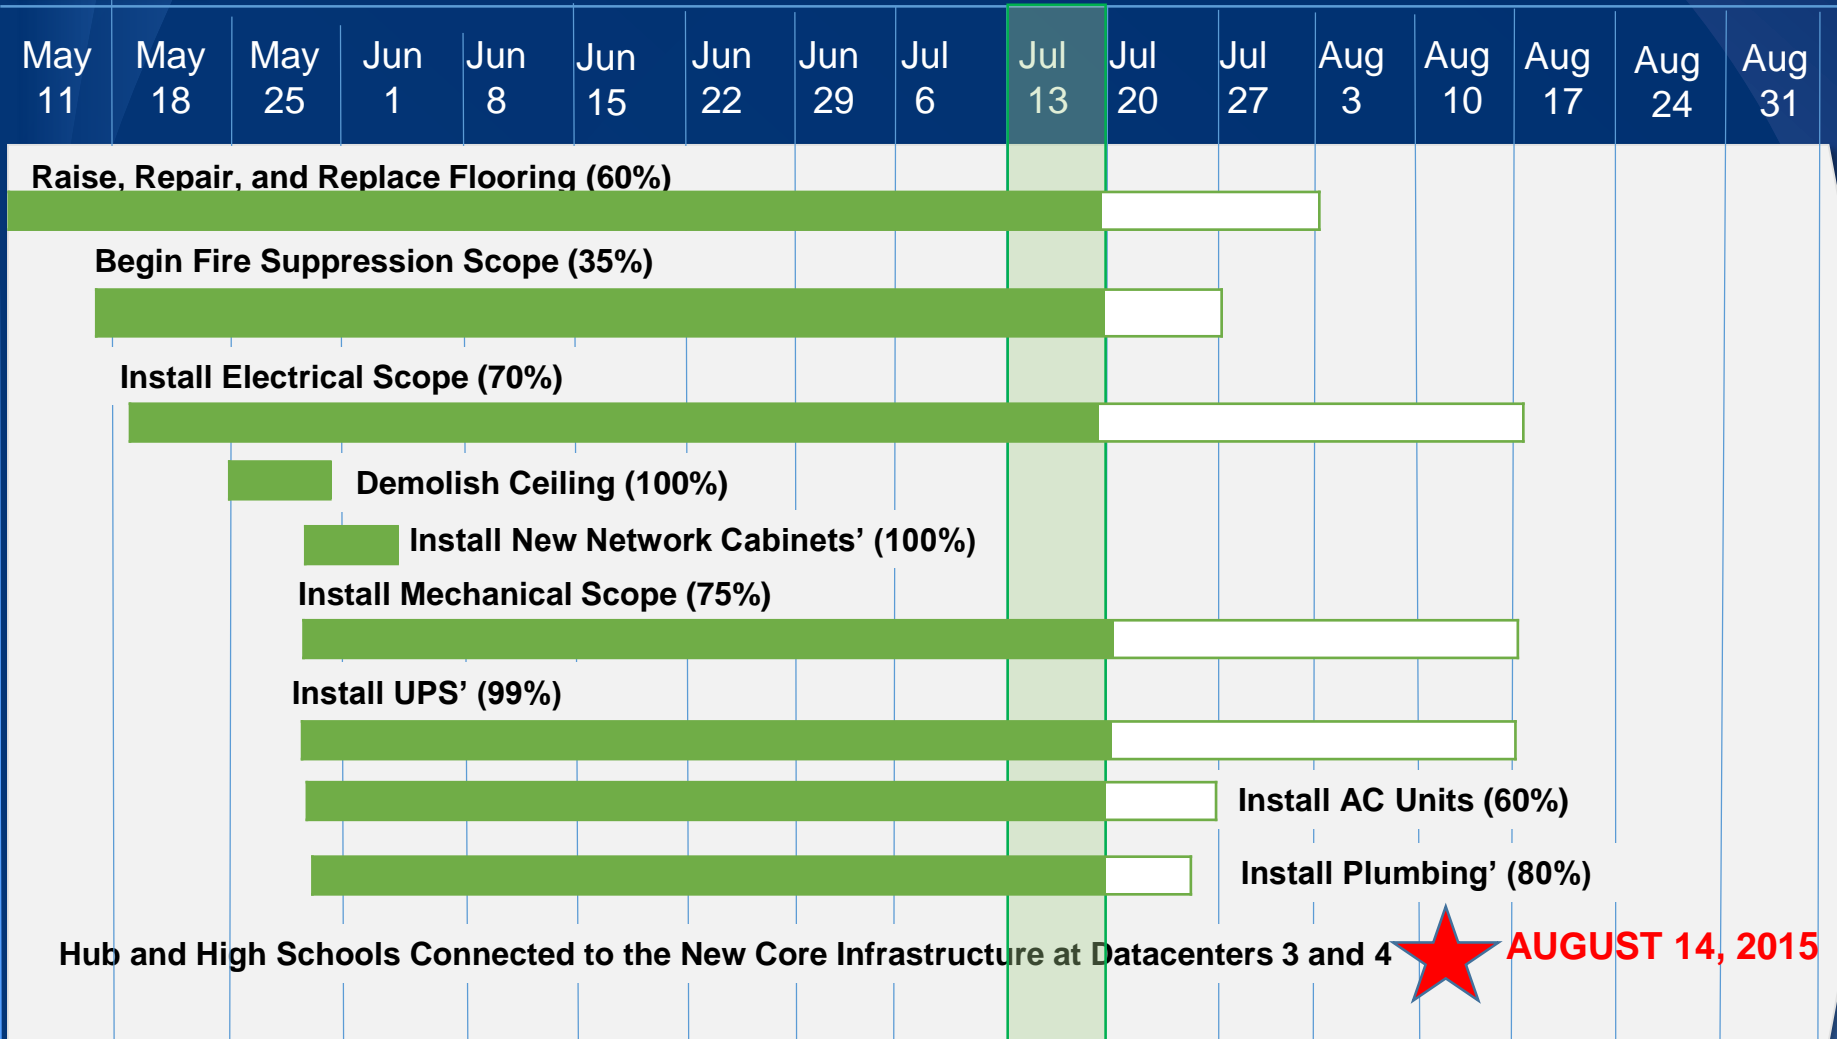

Bond Goal 2 Install Network Infrastructure Electronics
 Posted by: Frankie Jackson, Chief Technology Officer
 Post date: July 15, 2015




A PARTNER FOR THE LIFE CYCLE OF YOUR DATA CENTER



Goal 2

Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015

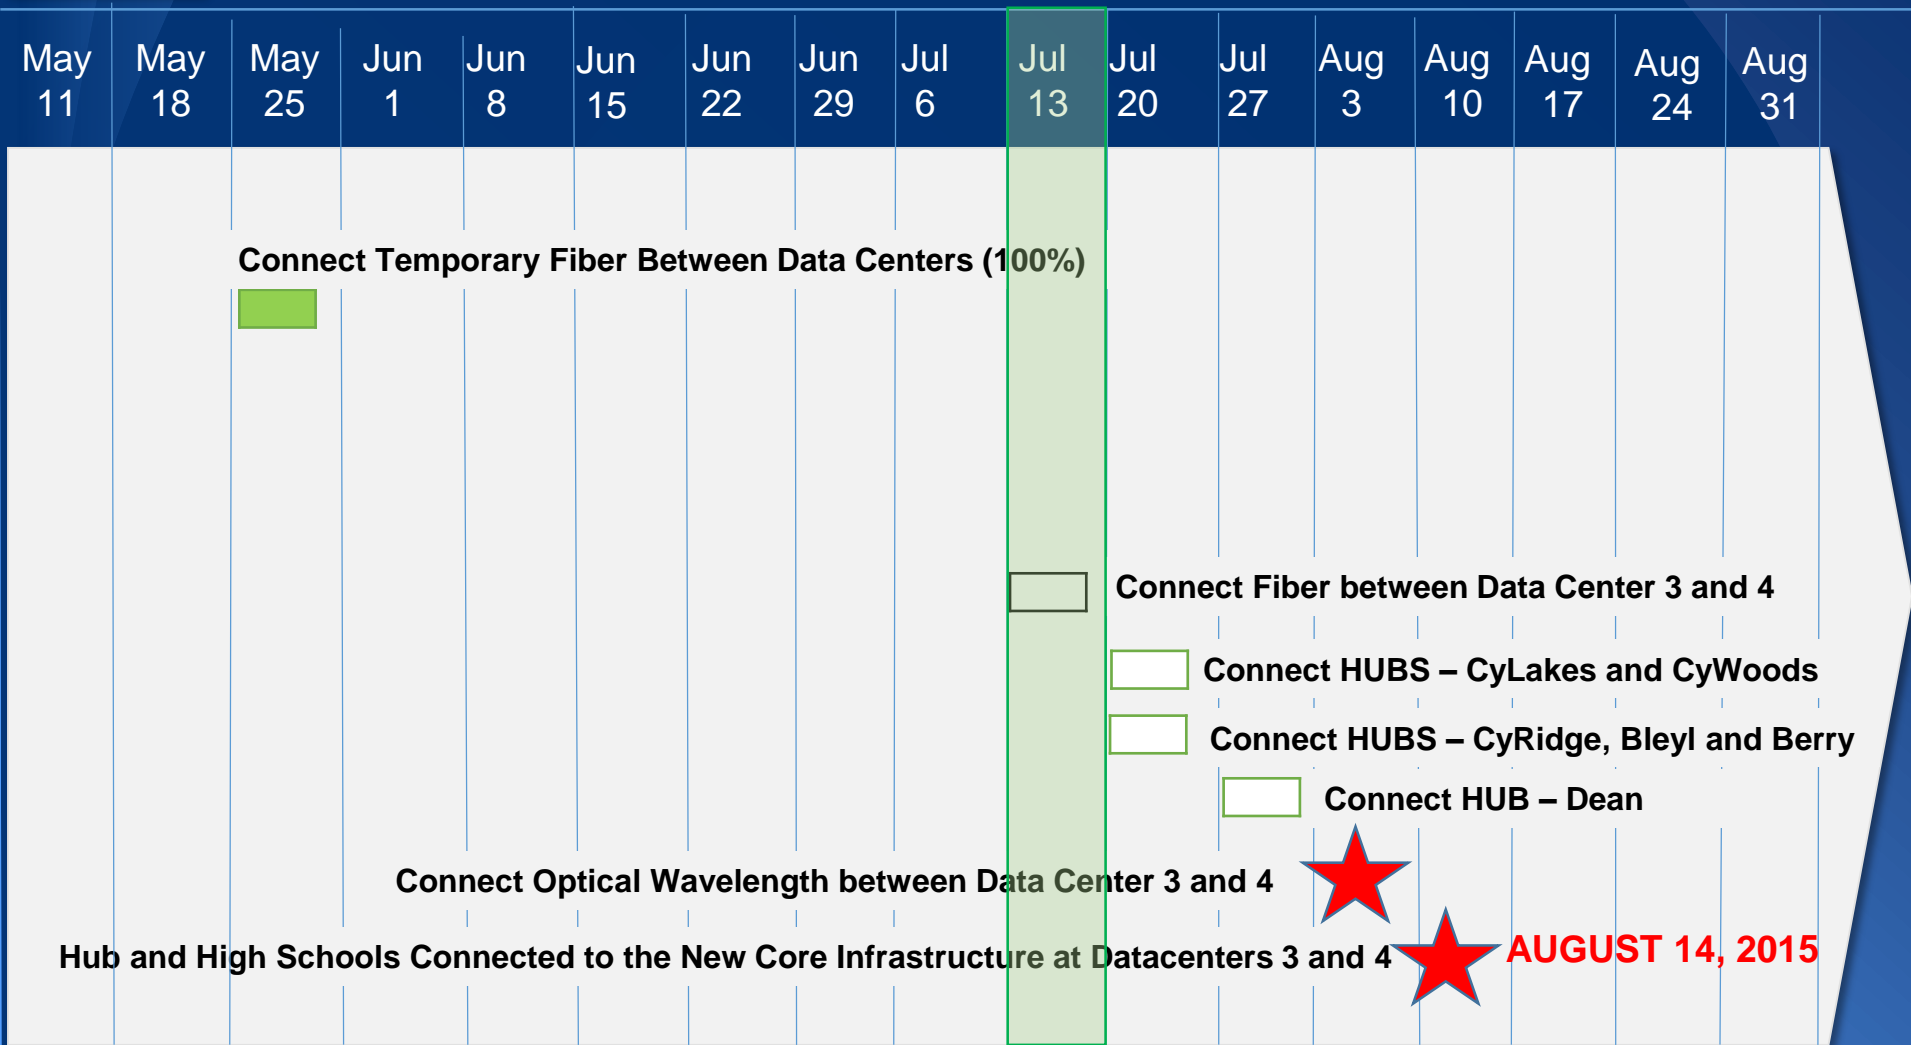


AUGUST 14, 2015





Goal 2

Network Electronics Infrastructure at the Data Center Core Level Continues for the Week of July 13, 2015



Conduct Technical Analysis and Prepare PO (100%)

Kickoff Meeting with SolidIT Networks

Install UPS' Following the Summer Network Installation Schedule

Cy-Lakes HS	80%	7/6/2015	7/9/2015
Cy-Woods HS	80%	7/13/2015	7/15/2015
Carlton Center		7/16/2015	7/16/2015
Cy-Fair HS		7/20/2015	7/23/2015
Bleyl MS	80%	7/20/2015	7/21/2015
Cy-Ridge HS		7/22/2015	7/27/2015
Cy-Falls HS		7/22/2015	7/27/2015
Dean MS		7/24/2015	7/24/2015
Cy-Ranch HS		7/27/2015	7/29/2015
Cy-Creek HS		7/28/2015	7/30/2015
Langham Creek HS		7/30/2015	8/4/2015
Windfern HS		8/3/2015	8/3/2015
Cy-Springs HS		8/4/2015	8/6/2015
Jersey Village HS		8/4/2015	8/6/2015

Hub and High Schools Connected to the New Core Infrastructure at Datacenters 3 and 4

AUGUST 14, 2015



Bond Goal 2 Install Network Infrastructure Electronics

Posted by: Frankie Jackson, Chief Technology Officer

Post date: July 15, 2015

