




Goal 2

# ECN Completes Another Week of Switch Conversions Andre, Hamilton, Birkes, Francone ES

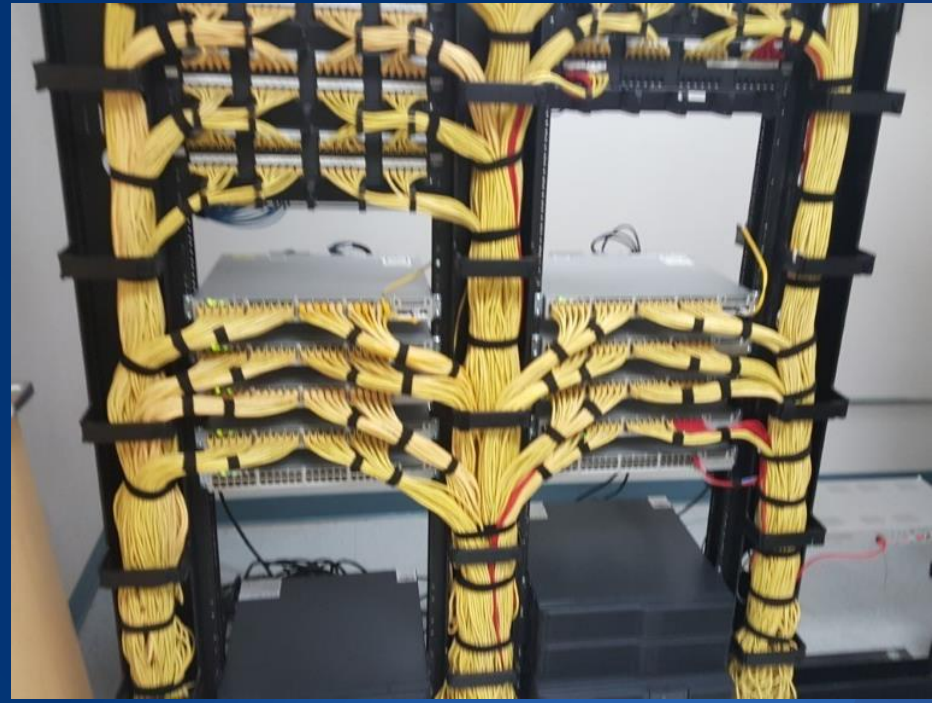

The ECN Team is implementing standards in the MDF/IDF campus closets. One of the first standards for each closet is cable dressing. Cable dressing ensures that cables are neatly arranged. **Anna Senties** and **Tony Rogers** have done a great job setting and managing the expectations for cable management with the Gigabit team during the previous campus switch conversions. Pictured above are **Tony Rogers**, **Elizabeth Montes**, and **Anna Senties** reviewing the cable dressing standards during Hamilton ES conversion on January 19, 2016. The goal is for all of ECN to follow the same method for dressing the cables in the MDF/IDF closets.



Goal 2

# ECN Completes Another Week of Switch Conversions Andre, Hamilton, Birkes, Francone ES



Since Monday was a district holiday, two schools were converted on Tuesday, January 19, 2016. **Elizabeth Montes** worked with David Deitsch and Britny Matthews from Presidio at Hamilton ES.

**Elizabeth** verified that all Cisco switches were deployed, that proper cable dressing procedures were followed, and that the new uninterruptible power supply (UPS) units were installed. The conversion completed shortly after lunch and then **Lillie Swearingen** from DII tested applications to ensure the switches were functioning properly.

**Thomas Hollister** worked with Presidio at Andre ES to complete the same conversion initiative.





Goal 2

# ECN Completes Another Week of Switch Conversions Andre, Hamilton, Birkes, Francone ES

B  
I  
R  
K  
E  
S



F  
R  
A  
N  
C  
O  
N  
E

On Wednesday, January 20, 2016, **Tony Rogers** managed the conversion effort at Birkes ES. Pictured above are members of the Gigabit team properly following CFISD’s cable management standards.

On Thursday, January 21, 2016, **Anna Senties** managed a successful conversion effort at Francone ES. By late afternoon the team had completed their second week of elementary conversions. Four additional campuses completed, thus bringing the total number of elementary switch conversions and UPS units deployed to ten elementary campuses.

**Bond Goal 2.3 Install Network Infrastructure Electronics – Campus Level**

Posted by: Paula Ross, Director of Network Infrastructure and Communications

January 19 - 21, 2016
