




Bane Elementary School Network Installation Update



Bane ES Principal, Dr. Carrie Marz, and her Staff

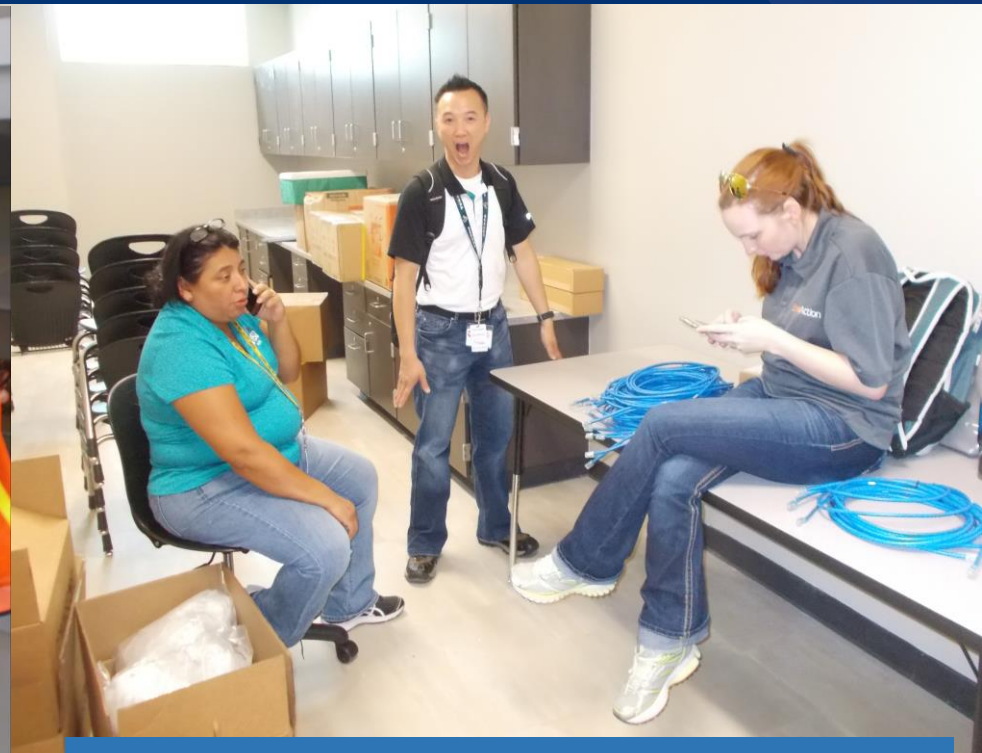

Anna Senties, Ray Leung and Britney Mathews
Prepping Cables for the Switch Installation

Michael Raspet was onsite at Bane Elementary this week to assist **Anna Senties** with preparations for the network installation. Michael stopped to take a picture of the Principal and her staff in their protective construction gear during a visit early in the week.



Bond 6.1

Bane Elementary School Network Installation Update



Anna Senties Performing a Little Clean Up Work



MCA and Anna Worked Together to get the Closets Completed

Michael Raspet and Anna Senties encountered several setbacks in the installation of the network closets at Bane Elementary including cut cables, damaged fiber and construction delays which pushed the completion date to the end of the last week prior to the start of school.




Bane Elementary School Network Installation Update

Michael Raspet and Anna Senties had to request a temporary A/C unit to cool the MDF closet electronics since the change order had not been processed to install the permanent unit. Delays in the cabling completion were attributed to the accidental removal of cabling in the old renovated portion of the school.



Temporary A/C Solution

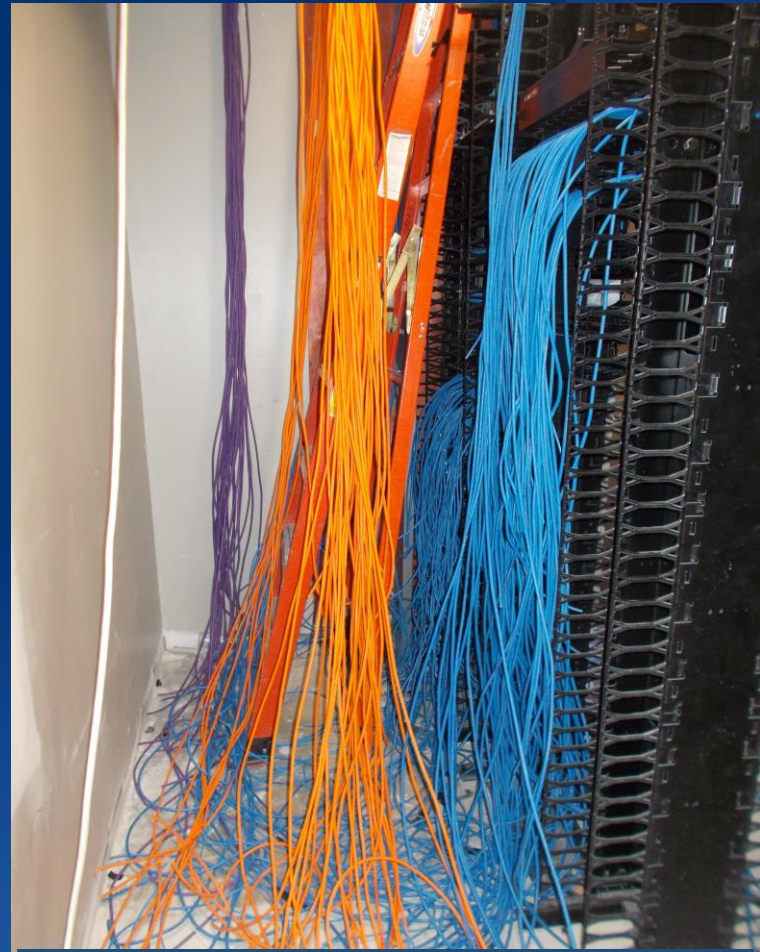

MCA Pulled Additional Cables after all of the Saved Cables were Accidentally Cut



Bane Elementary School Network Installation Update

Michael Raspet met Ray Lueng and Ken Wasko from Layer3 at Bane ES Friday morning to install wireless access points in the admin area and library to provide initial wireless coverage until they could return next week with the wire map and complete the installation.



Ray Lueng and Ken Wasko installing a wireless access point in the Bane library



Ken and Ray enjoying their morning at Bane ES
