




Bond 6.1

PSLightwave Site Survey for New Matzke Elementary

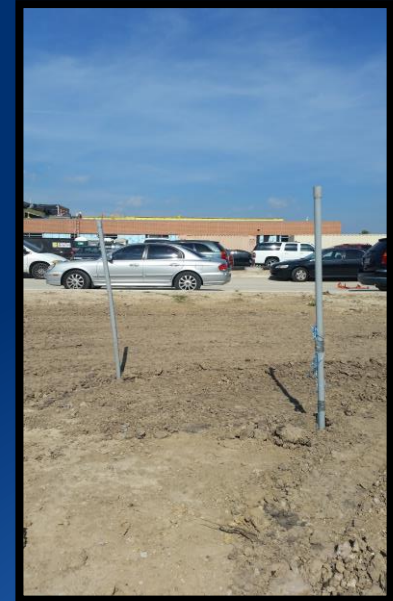

Michael Raspet met with Pete Cavazos from PSLightwave on Thursday at the new Matzke Elementary school to walk the proposed fiber optic route and determine whether any additional electrical work was necessary to ensure the project remained on schedule. Michael and Pete met with Courtney Abney Project Coordinator, Russell the contract electrician and Danny the General Contractor as they pointed out where the 4" conduit had been buried and where it was capped underground. Based on the original site survey the new route will remain the same except where the conduits were extended out from the MDF an addition few feet for sidewalk clearance.



PSLightwave Site Survey for New Matzke Elementary



End of the line for the conduit before turning and boring under Mills Road

Proposed fiber route from north end of property along Mills Road facing southeast.



Left pole holds the pull strings to the conduit from the MDF. Right pole is the end of the conduit running 530' along Mills Road.
